



"Everything in Excellence"

**WILLIAMS & THOMAS CONSTRUCTION CO.**  
4473 Progress Ave., Ste 1, Naples, FL 34104  
561.460.8525 | [www.wtconstruct.com](http://www.wtconstruct.com) | CGC1532780

## WEEKLY PROGRESS REPORT

Report No.	Date
# 13	09/06/2024

**CLIENT:**

**BOYNTON LANDINGS CONDOMINIUM ASSOC., INC.**

2309 North Congress Avenue, Boynton Beach, FL 33426

Attn: Susan Lorio | 561-732-4232

Email: [manager@boyntonlandings.com](mailto:manager@boyntonlandings.com)

**OWNER'S REP:**

**BUILDING MAVENS**

2309 North Congress Avenue, Boynton Beach, FL 33426

Contact: Matt

Email: [manager@boyntonlandings.com](mailto:manager@boyntonlandings.com)

**PROJECT: Exterior Facade Repairs and Window Replacement**

### COMPLETED WORK FOR WEEK ENDING: Friday, September 6, 2024

1. BLDG. 2307 — windows installed in units 11, 31, 16
2. Continued railing installations
3. Continued building deck floor and deck skirt (Saturday 9/7)
4. Prepped primed and painted the front of BLDG 2307
5. Continued building scaffolding on the rear side of BLDG 2307
6. Stucco on rear of BLDG 2307
7. Housekeeping to BLGD 2307 unit 26
8. One rain day; one holiday
9. Swing/Patio door installations in units: 11, 14, 15, 16, 17, 18, 26, 31, 32, 34
10. Installation of gutters right side of BLDG 2307
11. Started balcony work in BLDG 2307 changing 6x6 and damaged 2x10s

### EXPECTED PROGRESS WORK FOR THE FOLLOWING WEEK:

- ◆ Begin window installation on units 23, 32 and 24 BLDG 2307
- ◆ Siding repairs on BLDG 2307
- ◆ Continue installation of window trims
- ◆ Continue working on deck.
- ◆ Continue door installation on remaining units

\*See pictures, page 2

## WEEKLY PROGRESS REPORT — SUMMARY DETAILS

WORK DAYS	RAIN DELAYS	Holiday	AVG. DAILY MANPOWER	BLDGS WORKING ON
3	1	1	14	2307, 2305, CLUBHOUSE



**WILLIAMS & THOMAS CONSTRUCTION CO.**  
4473 Progress Ave., Ste 1, Naples, FL 34104  
561.460.8525 | [www.wtconstruct.com](http://www.wtconstruct.com) | CGC1532780

*"Everything in Excellence"*

## WEEKLY PROGRESS REPORT

Report No.	Date
<b>#13</b>	09/06/2024



**Stucco BLDG 2307**



**Paint BLDG 2307**



**Railing**



**Balcony**



## WEEKLY PROGRESS REPORT

**Report No.**


**# 13**

**Date**

09/06/2024



**Patio Door**

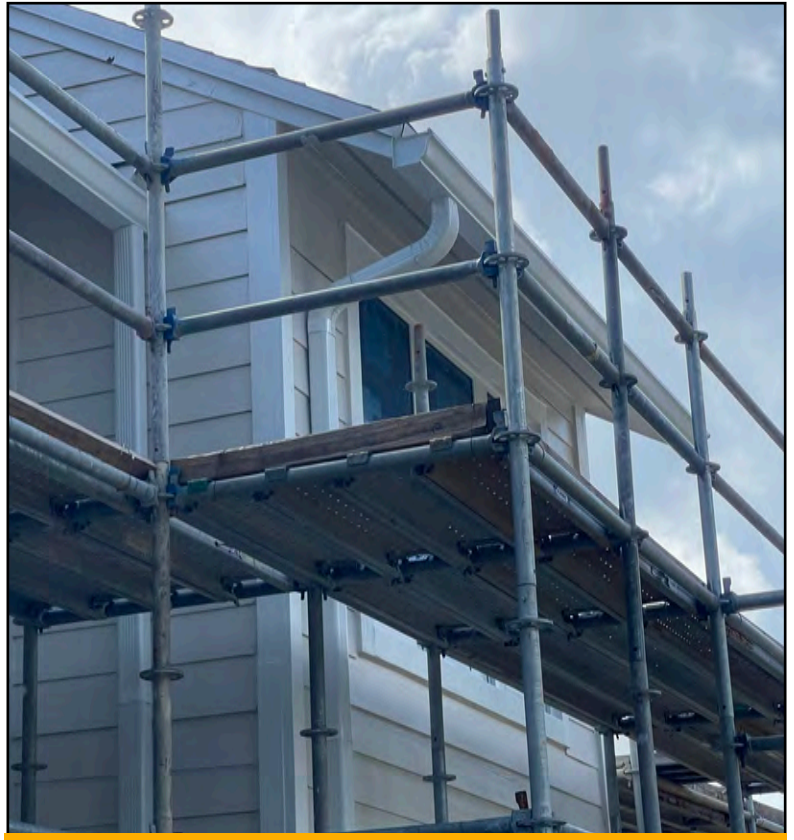

**Installation of Gutters BLDG 2307**



**Windows Unit 11**



**Windows Unit 31**
